

Group 3 - Space Complexity

Members:

**Kristy Mok, Ben Chalk, Corina Rivero Montiel, Euan Faller, Joel Cutler,
Luke Callen, Sam Ade Fowodu**


Timeline for Assessment 2: section 2b) iii) (Method selection and planning)

*The timeline is updated every Monday and Friday during our meetings and practicals.

Week 8:

18th - 22nd Nov

This week was the group selection phase. However, we did begin reviewing every deliverable and the game in more detail during the Friday practical session. This was to help us gain a brief overview of what needs to be changed (or not). In addition, we sorted out the management aspect and appointed our project manager to keep track of tasks and the general schedule. We also discussed the timeline and decided on our internal deadlines to ensure we deliver our assessment on time.

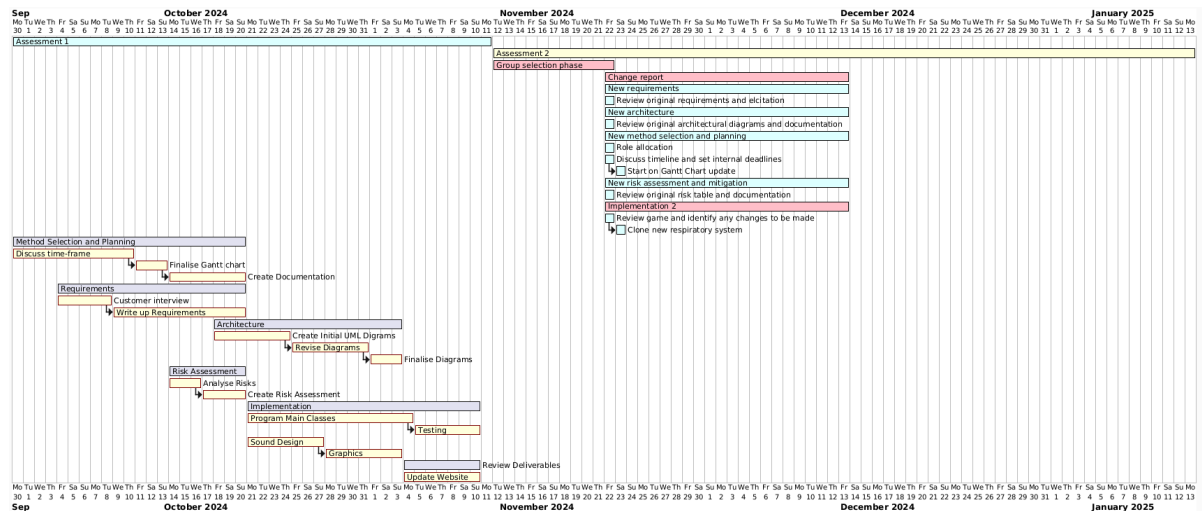


Week 9:

25th - 29th Nov

After asking our client and getting feedback from them, we were able to finalise what new requirements we needed to add and which original ones needed changing. E.g. We asked about the required events and what they would like to see, by doing so, we could use it to back up our events to be implemented.


As requirements were firmed, we could begin our implementation and update the requirements table and architectural diagrams. We cloned the new website, reviewed the existing code, and fixed the GitHub workflow file.

To keep things organised, we kept a document of our timeline and updated our systematic plan alongside the Gantt chart. These two will be updated regularly up until our internal deadline of 10/01/2025. We also adjusted the deadline for the change report as it's dependent on the method section, and in general, cannot be finalised until all deliverables from assessment 1 have been updated.

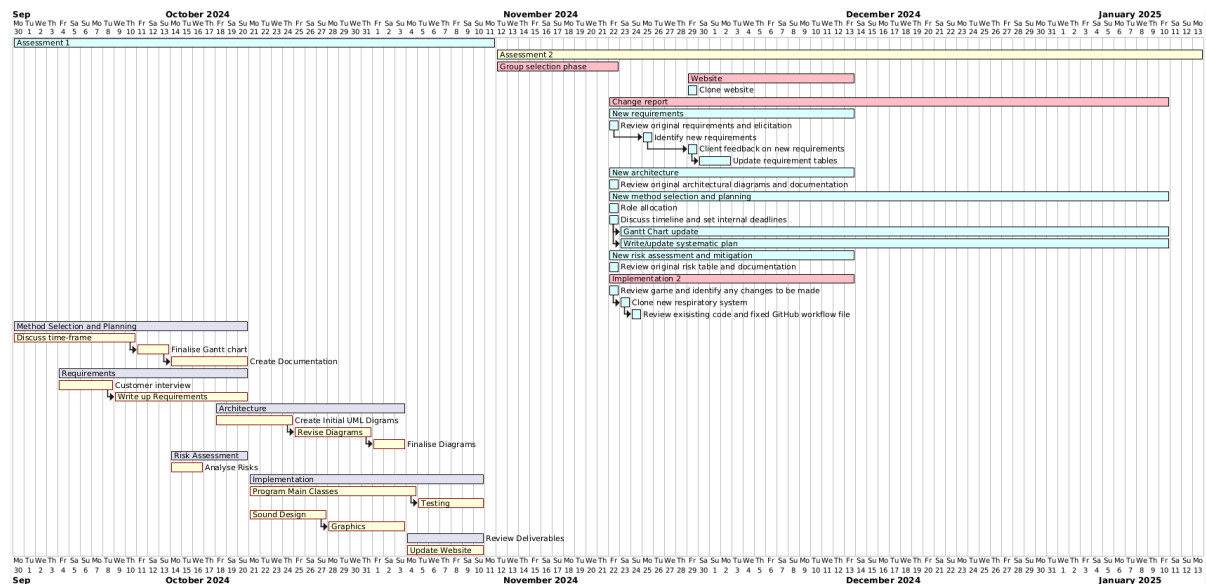


Week 10: 2nd - 6th Dec

We discussed how to identify and manage the changes we make to the deliverables, by which we decided to highlight the things we changed and added in different colours. We continued to implement new features like events and achievements to our UML architectural graphs and updated the change report with respective edits. We analysed and formalised the new risks and updated the change report accordingly. For implementation, we worked on adding new features to the game.

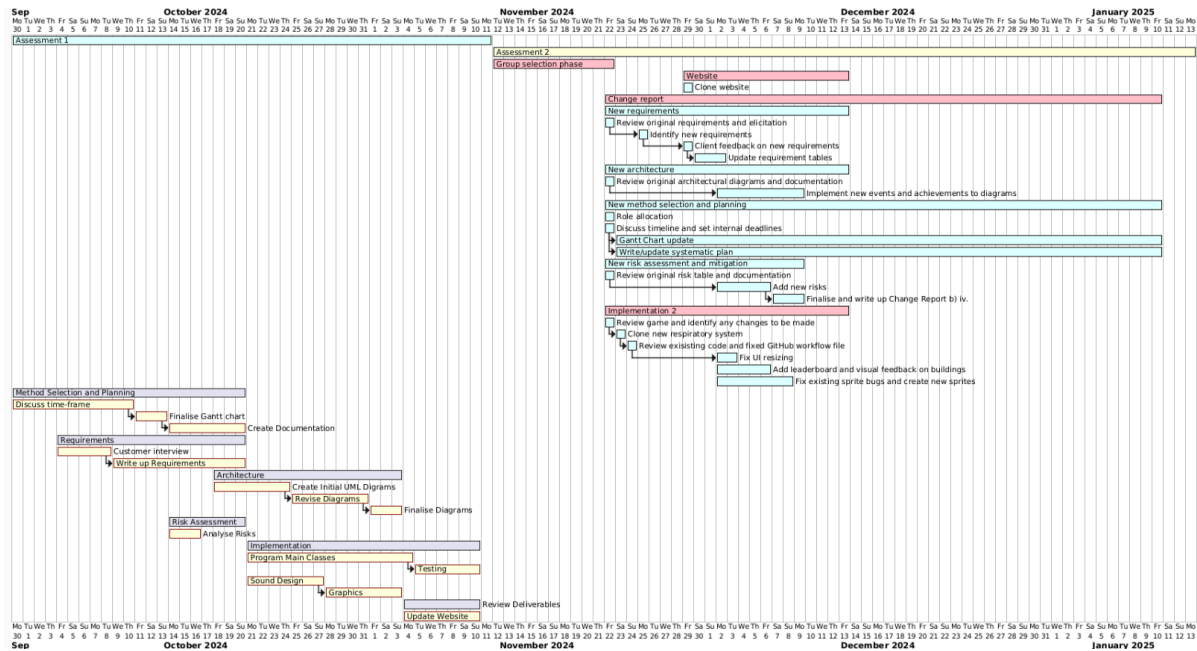

Week 11:
9th - 13th Dec

We discussed and planned our user evaluation, including preparing documents and creating a Google Form. By Friday (our last practical session), we successfully implemented the prototype version of our chosen game, following the assessment 2 product brief. This allowed us to begin our user evaluation phase, whereby we had 7 volunteers play the game and answer our short Google Form. The deadline for architecture is set to end alongside finishing version 2 of the game with feedback-focused updates, to ensure the architecture reflects and represents the implementation fully.

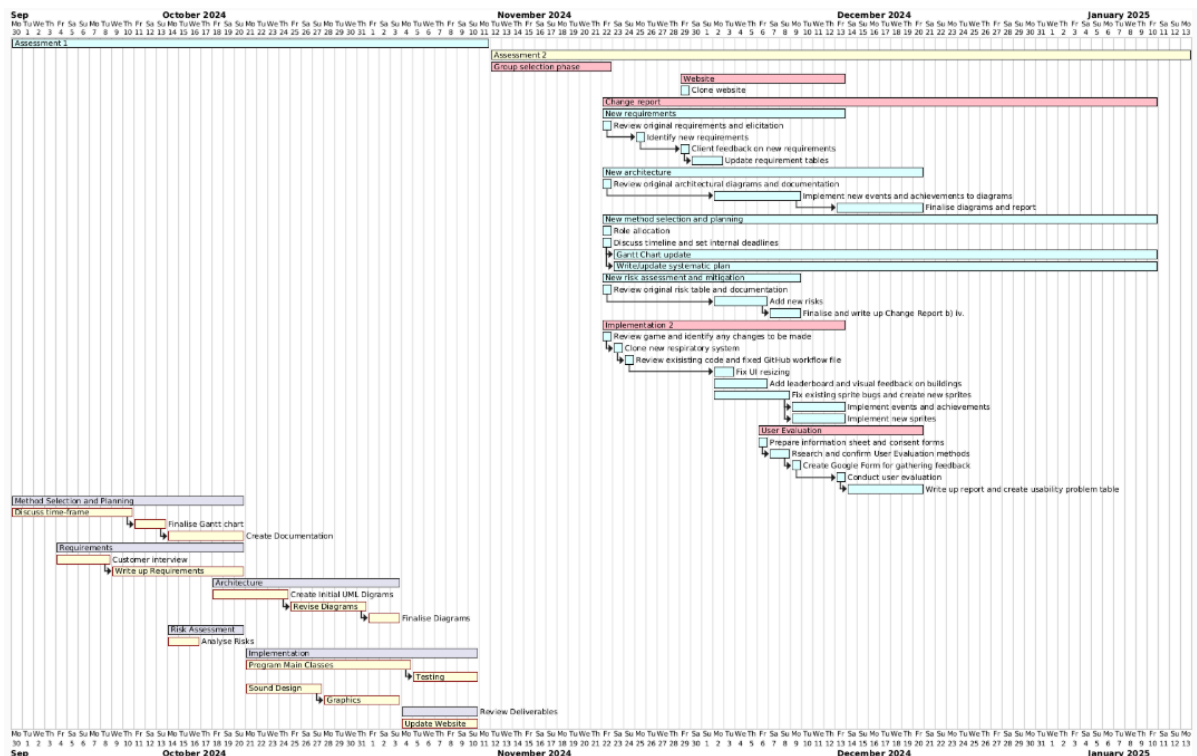


Week 12:
16th - 20th Dec

From the open-ended feedback gathered by our Google Form, we were able to pinpoint specific areas that needed fixing or extra details to add to allow for a better user experience. The implementation and architecture sections were finalised simultaneously.

For the requirements section, we revised (based on the user feedback) the requirements table and added extra research evidence. This enabled us to wrap up the change report for its respective section.

Our user feedback was compiled and analysed to create a usability problem table with scales to measure and prioritise the problems we collected; the user evaluation report was completed in the set timeframe.

Section 2a of the change report was written up this week.

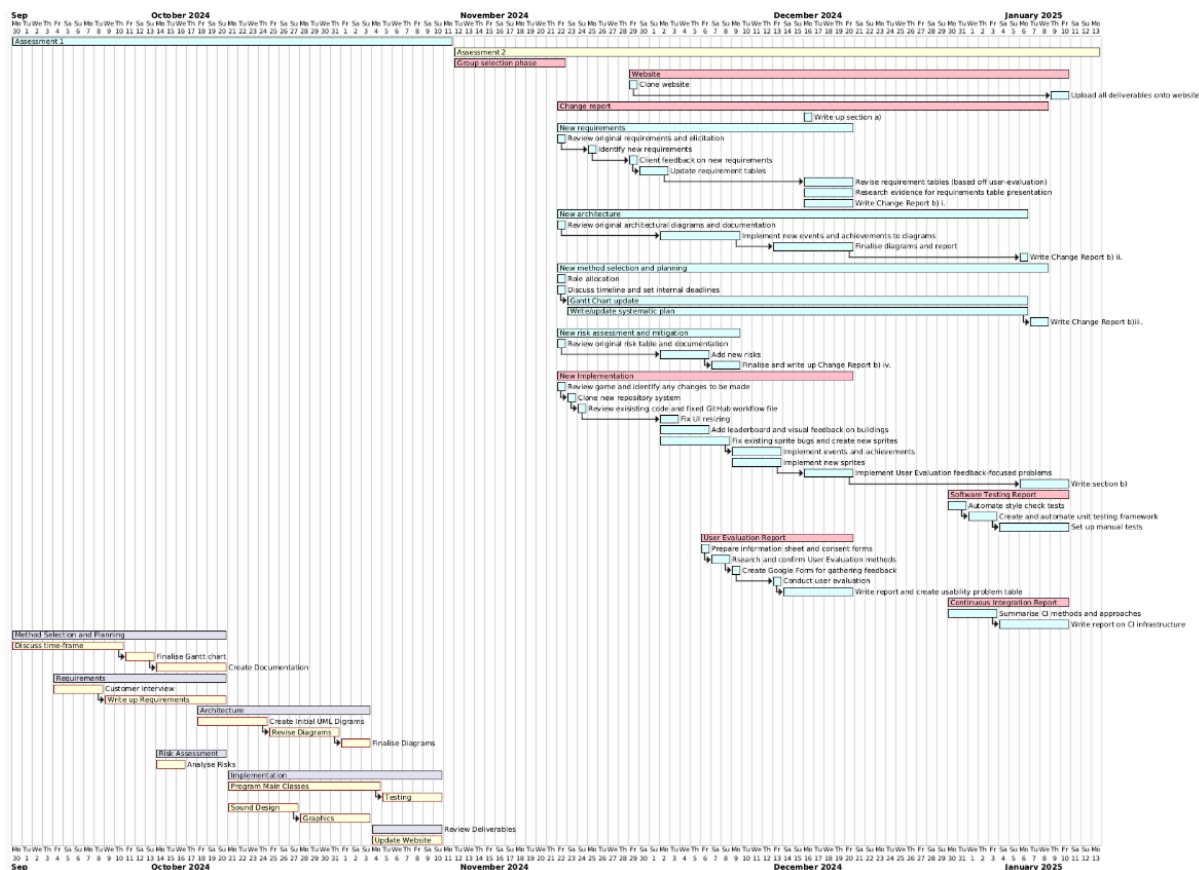

Week 13:
23rd - 27th Dec


As this was Christmas week, most of the team was busy due to personal commitments, so little was achieved. Hence, there is no update on the Gantt chart.

Week 14:
30th Dec - 3rd Jan

Our team's progress slowed down significantly due to a lack of communication and slow responses from members as it was still the holidays. This meant that we started on the latter sections of Assessment 2 later than we'd hoped.

Throughout the implementation process, our team have consistently practised continuous integration, whereby our members updated and shared their progress almost daily and multiple times a day. This week we have started writing the first part of the continuous integration report.

Started on software testing and added style check testing and automated it. Afterwards, we manually went through the entire project refactoring it to pass all the style tests. The framework for unit testing was created and also automated during this week. We had three members working on software testing as a part of the implementation section, hence there was a handover, resulting in a delay in the workflow for this area.

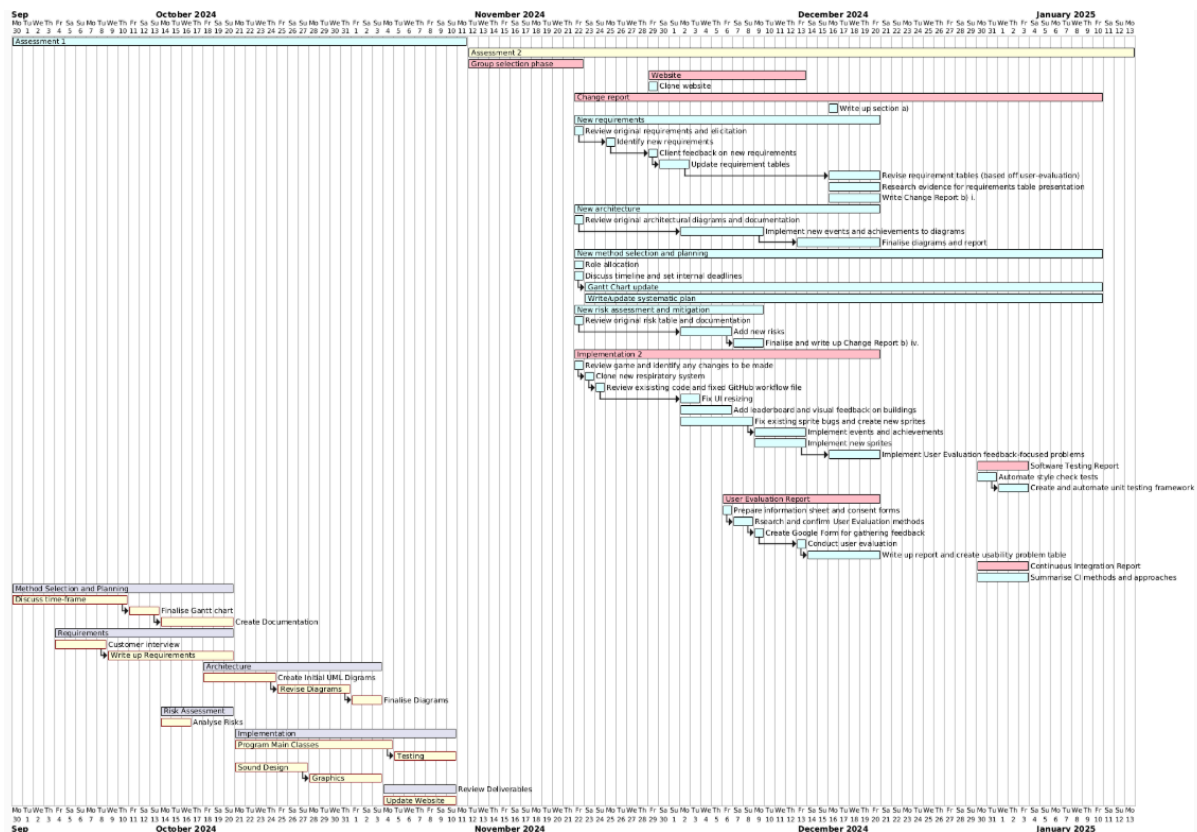

Week 15:
6th - 10th Jan


This week marks the final week of our Assessment 2 timeline as we have set the 10th Jan as our internal deadline for our submission.

This also means that the Methods and planning section will be finalised this week (as the Gantt chart will be done), along with its respective change report section.

We are still working on Software Testing, where we are writing the report and continuing to set up unit and manual tests along with its test plans.

To finish up our Continuous Integration section, we are writing up the CI infrastructure we have set up for our project.

After finalising all deliverables (such as the remaining implementation part b and architecture change report), we will upload everything onto the website.

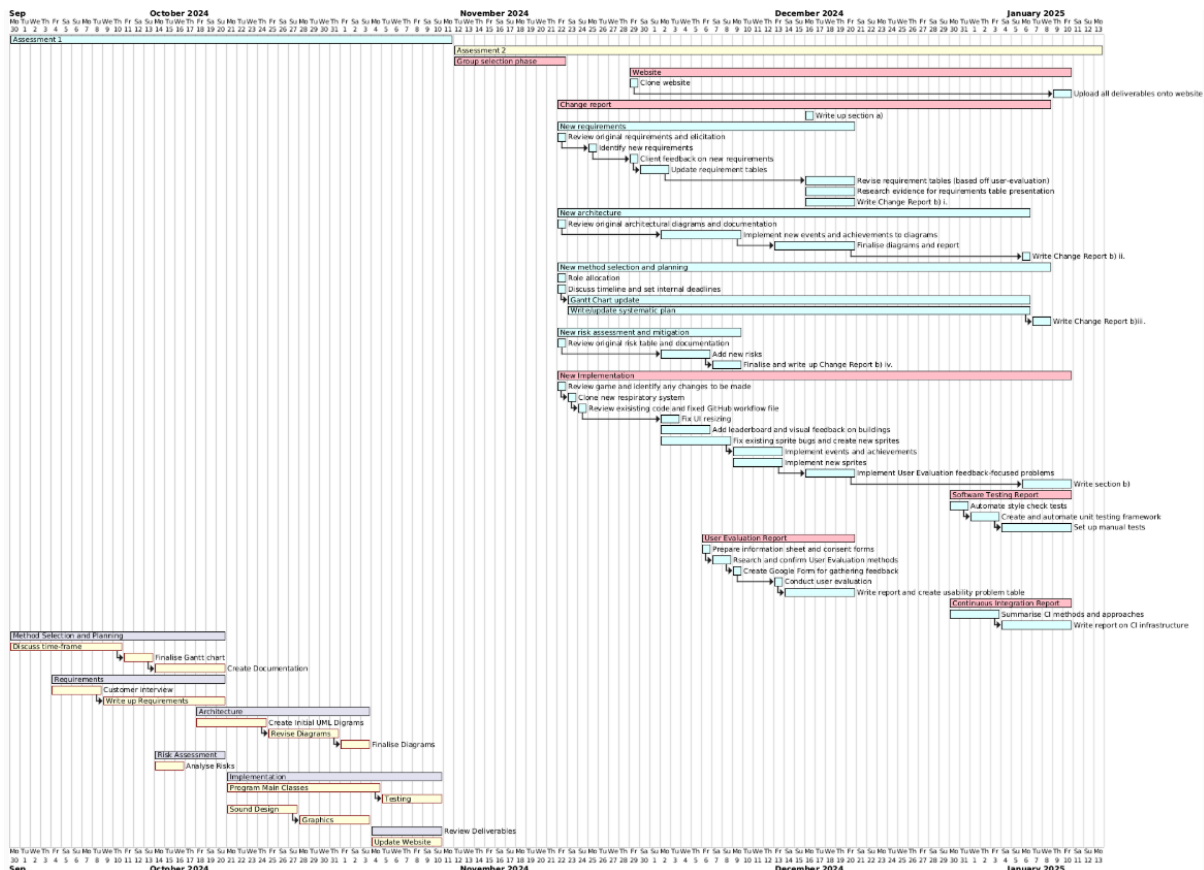

Week 16:
13th Jan

We set our internal deadlines at the beginning of Assessment 2 to support a timely submission. We managed to submit our project three days before the external deadline. There is no update to the Gantt chart as we have now finished Assessment 2.
